WESTBAY WELL COMPLETION DIAGRAM
BLM-32

Elevation of Inner Casing: 4597.20' a.m.s.l.

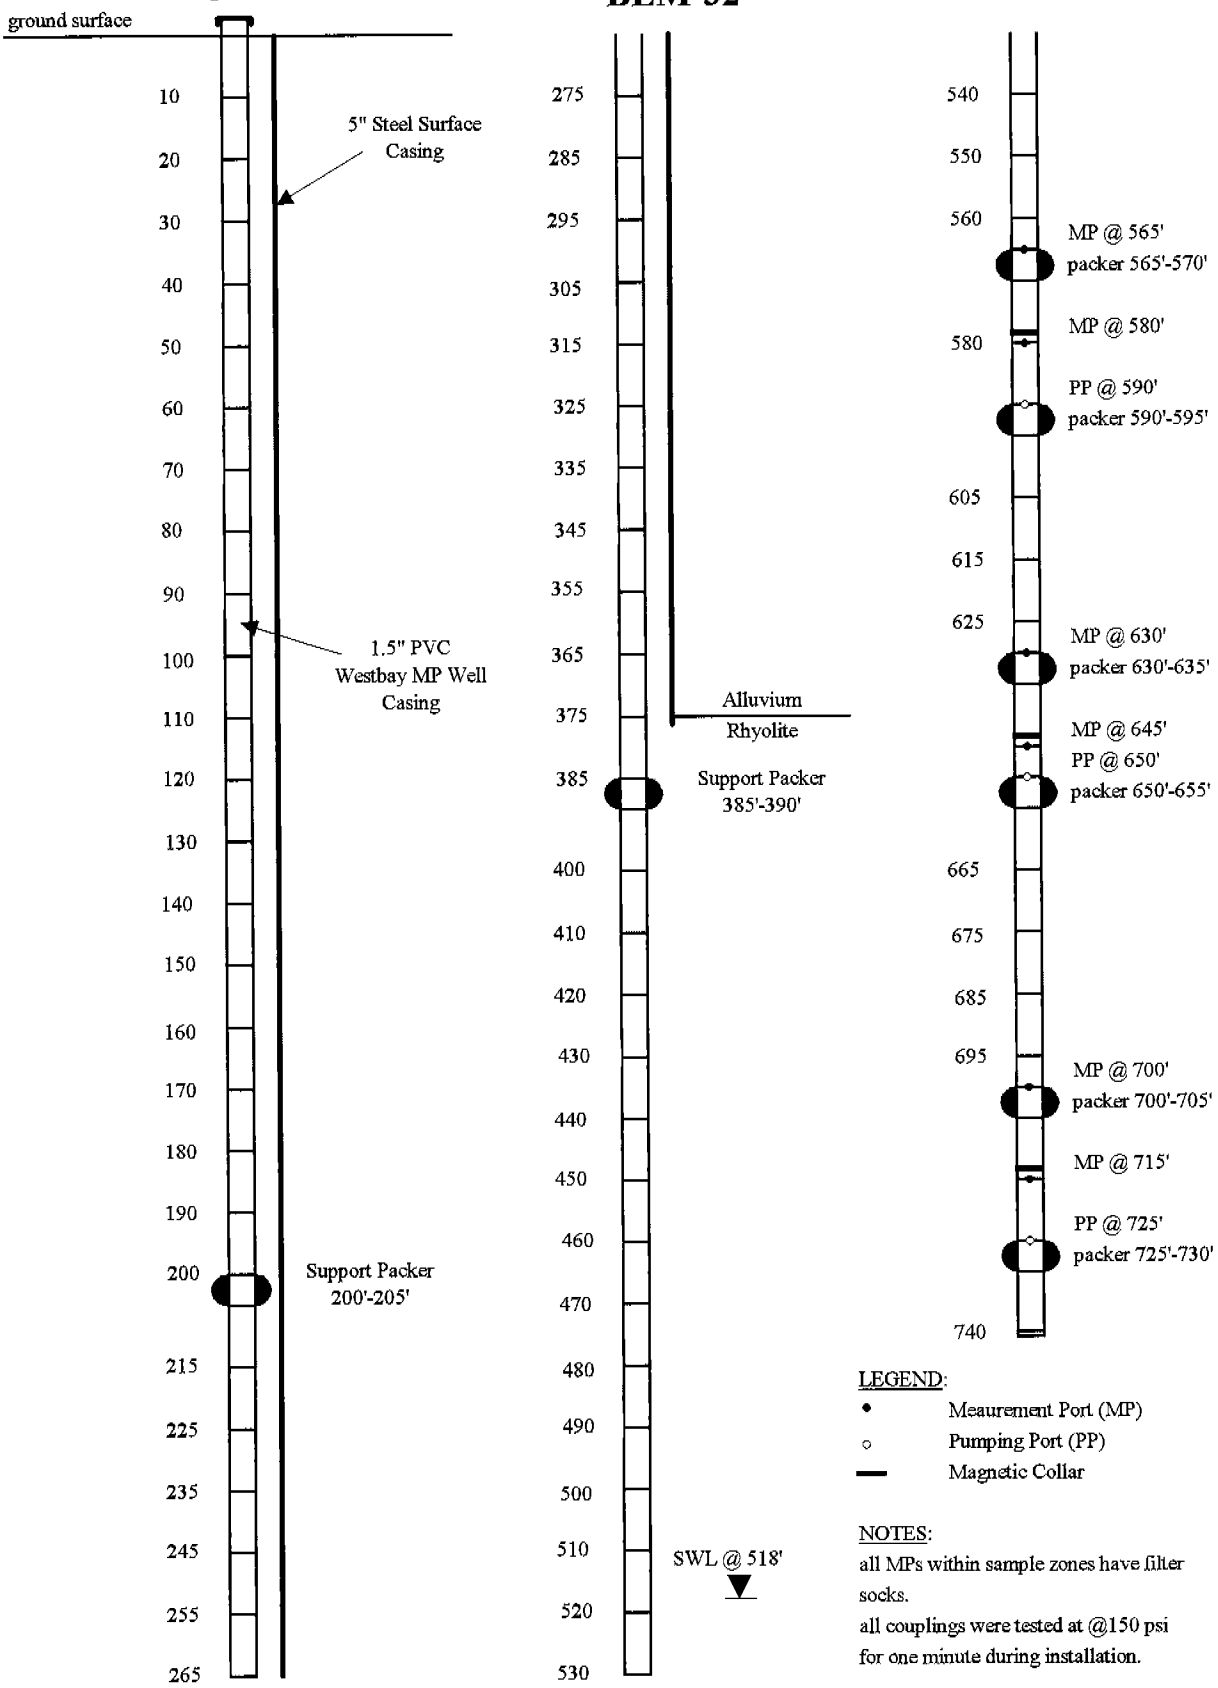

LEGEND:

- • Meaurement Port (MP)
- ○ Pumping Port (PP)
- — Magnetic Collar

NOTES:

all MPs within sample zones have filter socks.

all couplings were tested at @150 psi for one minute during installation.

Installation Date: 6/18/97

Installed By: ATSC

Elevation (BC): 4595.84' a.m.s.l.

Drawn/Checked By: PSE/MGC

MP Depth: 740'

Borehole Depth: 744'
